


# Architectural Aesthetics / The Art of Craft

## Generic Client Project PERT Network / Time Line

print: 8x10 landscape 75%

This is a work flow chart of a typical project from start to finish to create The Art of Craft ornamental gates for any given client. Each box represents a task description, the duration - amount of time (in weeks) that that task typically takes to be completed, the start date of that task, the resource - primary responsible party, and the completion date for that task.

If the project were to commence on Jan. 1, the project would be complete on May 9. (17 weeks) (given typical conditions). (Concept, Design, Client approvals, and progress payment times, handled efficiently, can shorten the process by as much as 5 weeks or delay the process considerably.)

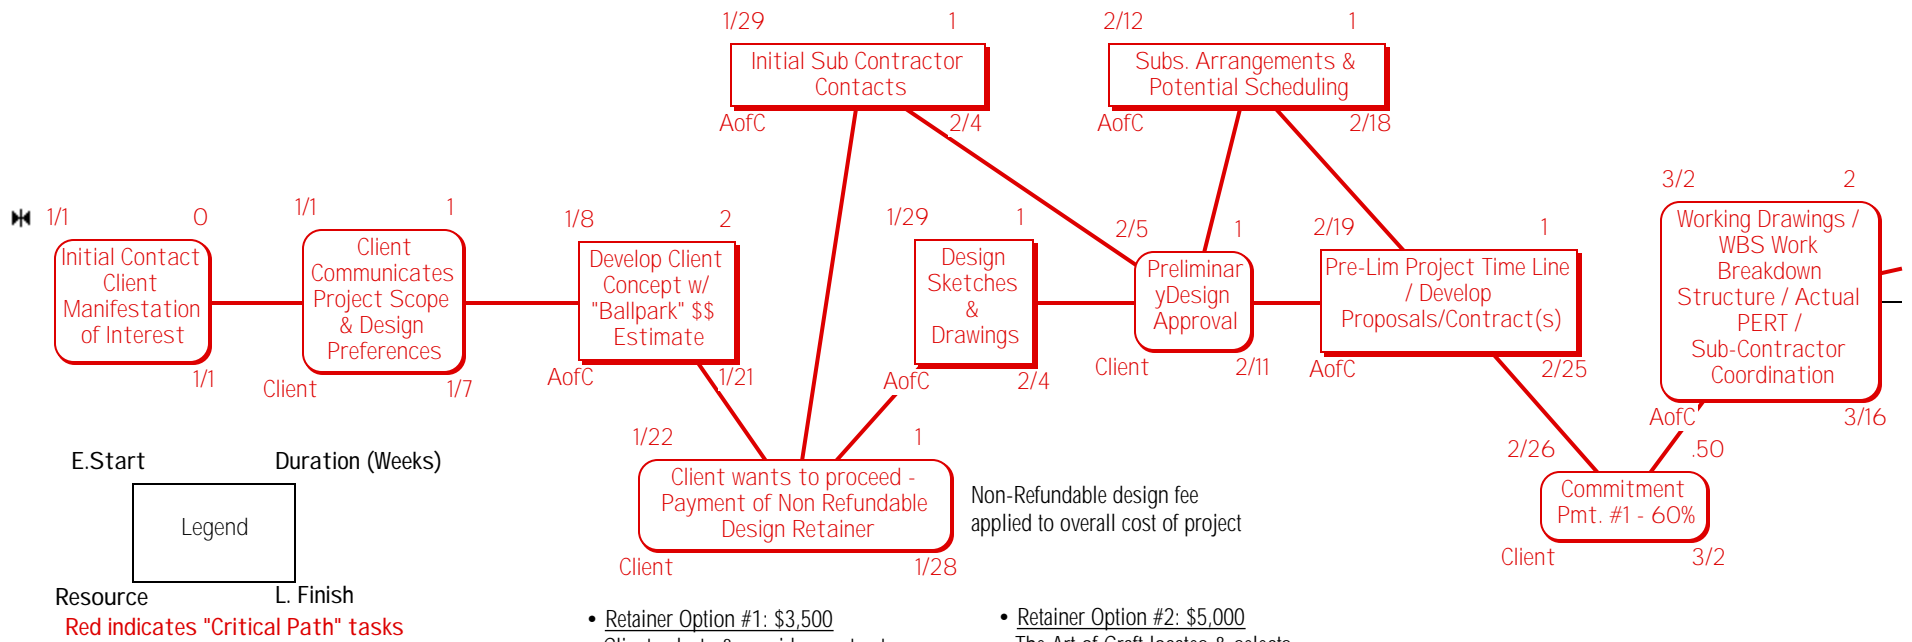

- Retainer Option #1: \$3,500  
 Client selects & provides contractor for mechanical elements of project. The Art of Craft provides only art insert.

- Retainer Option #2: \$5,000  
 The Art of Craft locates & selects contractor for mechanical elements of project.

